

JULY 26, 2011 - NORTH ROAD SEWER PROJECT UPDATE

Spazzarini Construction has installed approximately 4,300 feet of gravity sewer as of Tuesday afternoon, July 26th. Additionally, a total of 20 Sanitary Manholes have been installed.

While installing lengths of 10 inch PVC sewer pipe in the area of Bassdale Plaza at 148 North Road we encountered what we believe to be weathered gasoline. We convened a meeting of the Contractor, Ed Spazzarini, Plant Superintendent Art Enderle III, and the Resident Engineer, Jay Ussery of JR Russo.

We decided to stop excavation at this point to place a call to Paul Tanner, a Licensed Environmental Professional with the Engineering firm of O'Reilly, Talbot and Okun (OTO) Associates of Manchester Ct.



Spazzarini Construction Company

Paul Tanner then contacted Robert Shuler of CT DEP to inform him of the discovery. Mr. Shuler visited the site and conferred with Paul Tanner. They both agreed that there is no indication of a current Underground Storage Tank (UST) failure, and it appears this is an old existing situation.



Eastbound along Rt 140 / prior to Bassdale Plaza

We estimate that there may be up to 200 tons of wet odorous soil to be remediated along this project stretch. We plan to use the existing construction staging area for placing the soils to be treated. Environmental Services Incorporated (ESI) of South Windsor is being retained to assist with manpower and equipment to control / contain water and assist with trucking and disposal once the material is ready to be transported to an approved disposal site.



Spazzarini Construction along Route 140

JULY 26, 2011 - NORTH ROAD SEWER PROJECT UPDATE




WPCF Operator Marc Brennan is all smiles at the existing North Road Pump Station location, with the USDA announcement.

We will be removing approximately 100 ft of recently installed 10 inch PVC pipe and replacing it with 10 inch ductile iron pipe with viton gaskets that are not affected by petroleum. We will continue with another 200 ft of ductile iron pipe until the next manhole, at which time we feel we will be out of the contamination.

On Monday August 8th OTO associates will be on site to perform a safety meeting, monitor vapor levels, monitor with a gas detection meter, and use metering to determine soils condition. The contaminated materials will be stockpiled and covered at the staging area until such time as they are approved for transport by ESI to an approved reclamation facility.

We believe this clean up will take from Monday August 8 through Tuesday August 9th to complete. Spazzarini Construction was able to begin work on the service laterals from the main line to the property line so we have not lost any construction time.

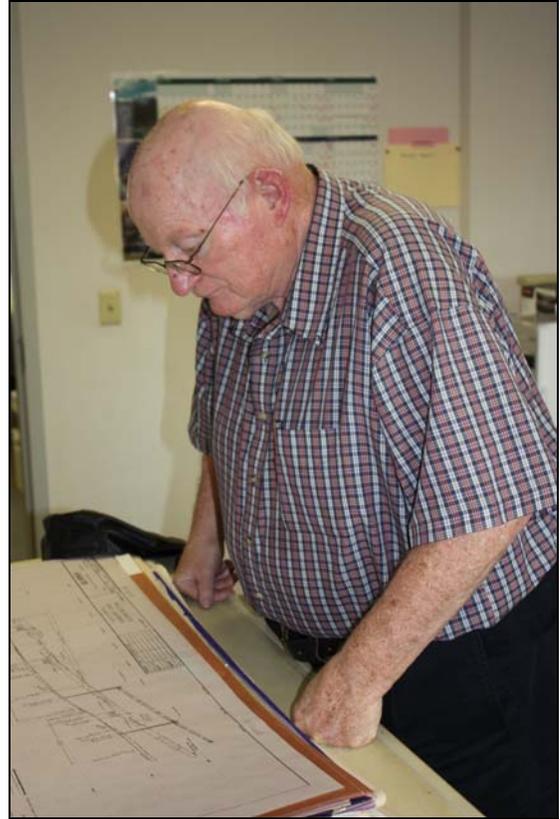

WPCA Vice Chairman Thomas Davis looking over plans for the North Road Sewer Project.



WPCA Chairman Paul Anderson addressing residents at a WPCF Informational Session.

North Road Project Update - July 26th, 2011

